

Deliverable 1

Sprint Planning Facilitation Guide

Create a step-by-step guide for running a **2-hour Sprint Planning session** for a team of 5.

The guide should include:

- Meeting agenda
- Activities for each stage
- Questions to ask the team
- Outputs to capture
- Time allocation

Published just now   Edit  Share  ...

Sprint Planning Facilitation Guide

By Rudraksh Mishra  Listen  Add a reaction

Sprint Planning Facilitation Guide

Meeting Information

Attribute	Value
Sprint Length	2 Weeks
Team Size	5 Members
Duration	2 Hours

Objective

The objective of Sprint Planning is to determine what work will be completed during the sprint, define a shared sprint goal, and create a plan for delivering the selected backlog items.

Sprint Planning Agenda

1. Sprint Planning Kickoff (10 Minutes)

Purpose

- Review sprint objectives
- Confirm team availability



Summarize page 

Work link:

<https://rudraksh.atlassian.net/wiki/external/ZTA0MWI1NzhkOTEwNGQwM2E2NTEwN2U1Mjl1MDYxYzY>

Deliverable 2


Jira Sprint 1 Screenshot

Show: Stories selected for Sprint 1

Team capacity documented:

Team Capacity = 40 Story Points

Sprint Goal written and visible

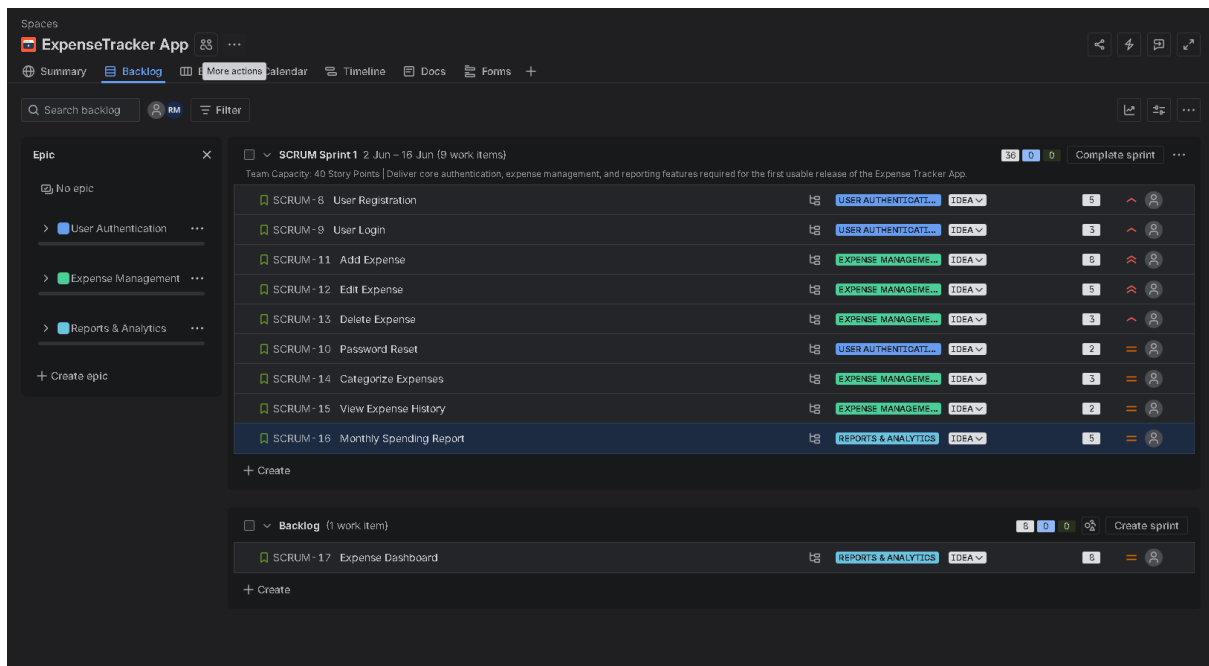

Work link:

<https://rudrakxh.atlassian.net/jira/software/projects/SCRUM/boards/1/backlog?epics=visible&atlOrigin=eyJpIjoiNTkxMzJhYzljY2MyNDQ5ZmFjMzVkYmUzODExNGNhZjkiLCJwIjoiY9oi>

Deliverable 3- Short Note:

What Happens When Teams Over-Commit During Sprint Planning and How to Prevent It

Meaning of Over-Commitment

Over-commitment occurs when a team selects more work for a sprint than it can realistically complete within the available time and capacity. This usually happens when capacity, velocity, dependencies, or complexity are underestimated during Sprint Planning.

Consequences of Over-Commitment

1. Missed Sprint Goals

When too much work is committed, the team may fail to complete the planned stories. As a result, the sprint goal is not achieved, and the expected business value is delayed.

2. Increased Carry-Over Work

Incomplete stories must be moved to the next sprint. This creates backlog accumulation, disrupts planning, and reduces team efficiency.

3. Team Stress and Burnout

Teams often try to compensate for excessive commitments by working longer hours. This can lead to stress, reduced morale, and lower productivity.

4. Reduced Predictability

Repeated over-commitment makes it difficult to accurately forecast future sprint outcomes. Stakeholders lose confidence in delivery estimates and project timelines become unreliable.

How to Prevent Over-Commitment

1. Use Historical Velocity

Teams should review their previous sprint velocity and use it as a guide for selecting work. If a team typically completes 35 story points, committing to 50 story points is risky.

2. Calculate Capacity Accurately

Before selecting stories, the team should consider vacations, holidays, meetings, training sessions, and other factors that reduce available working time.

3. Leave Buffer for Unexpected Work

Not all work can be predicted. Teams should reserve a small portion of their capacity to handle bugs, support requests, and unforeseen issues.

4. Break Large Stories into Smaller Stories

Large stories often hide complexity and uncertainty. Splitting them into smaller, manageable stories improves estimation accuracy and reduces risk.

5. Commit Conservatively

Teams should focus on achievable commitments rather than optimistic targets. Completing planned work consistently is more valuable than repeatedly missing sprint goals.

Conclusion

Over-commitment can result in missed goals, unfinished work, team stress, and unreliable planning. Teams can avoid these problems by using historical velocity, calculating capacity accurately, maintaining a buffer for unexpected work, breaking down large stories, and making realistic sprint commitments.
