

Deliverable 1: Sprint 2 Simulation Document

Sprint 2 Simulation

1. Backlog Grooming

The Product Manager and team reviewed the backlog, clarified requirements, estimated effort, and prioritized items for Sprint 2.

Backlog Item	Priority	Story Points
Dashboard Overview	High	8
Monthly Spending Report	High	5
Expense Search	High	5
Expense Filters	High	3
Export Expenses to CSV	Medium	5
Expense Categories Enhancement	Medium	3
Profile Management	Medium	5
Notification Preferences	Low	3
Dark Mode Support	Low	2
Help & Support Page	Low	2

2. Sprint Planning

Team Capacity


Work Link:

<https://rudrakxh.atlassian.net/wiki/external/OThmYmU4ZWJjNmY3NDM5NmI5YmZINWQ5Y2VkMzU2NzA>


Deliverable 2: Sprint 2 Simulation Document

Jira Board Screenshots


Sprint Start

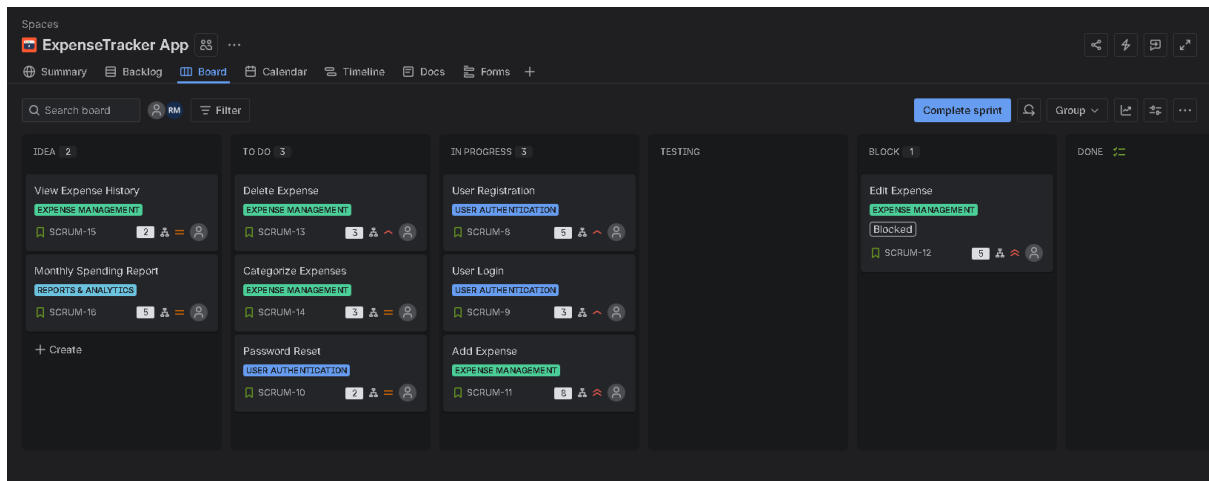

Sprint Mid

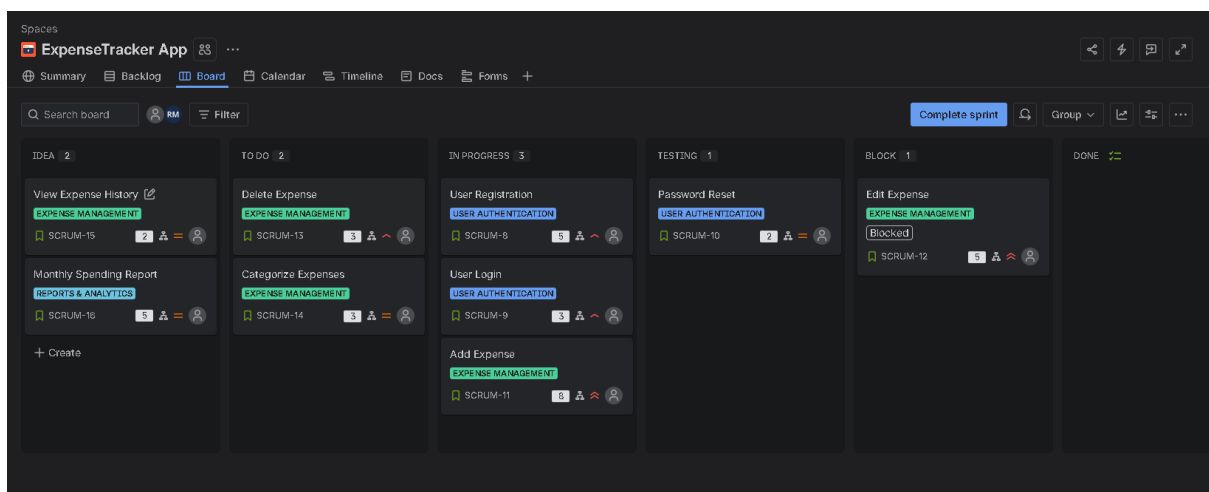

Sprint end

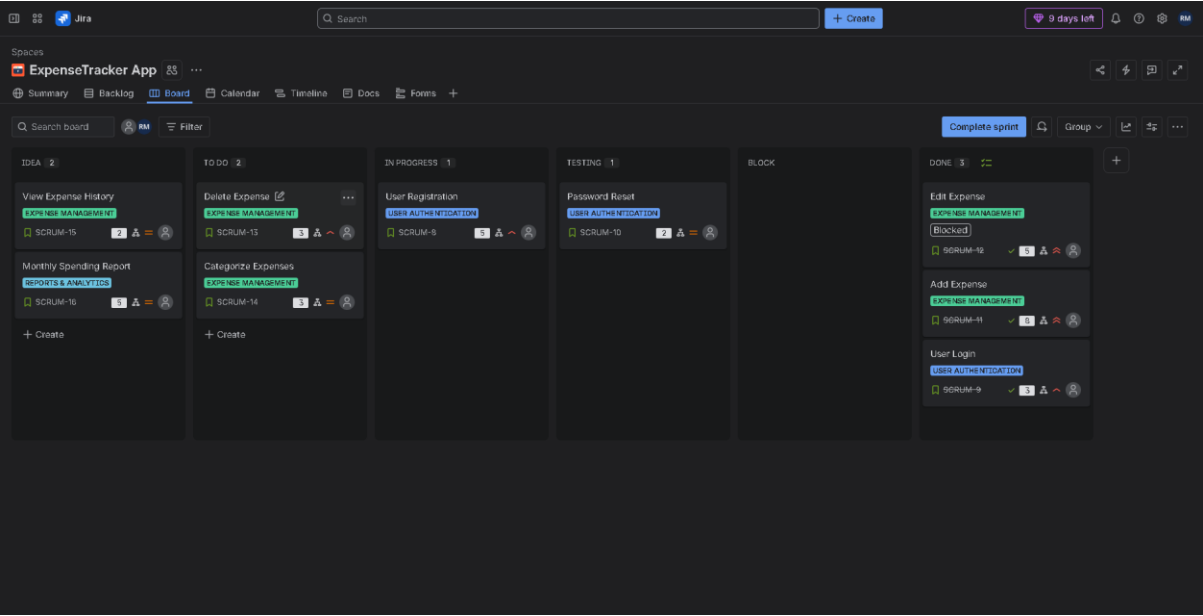

Deliverable 3: Sprint 2 Summary Document

Sprint Information

Sprint: Sprint 2

Project: Expense Tracker App

Sprint Duration: 2 Weeks

Sprint Goal

Deliver reporting and expense management enhancements that improve user visibility into spending behavior and enable more efficient expense tracking.

Completed Work

The following stories were successfully completed during Sprint 2:

- Dashboard Overview
- Monthly Spending Report
- Expense Search
- Expense Filters
- Export Expenses to CSV
- Profile Management

Total Completed Story Points

28 Story Points

Incomplete Work

The following story was not completed during Sprint 2:

- Expense Categories Enhancement

Story Points

3 Story Points

Reasons for Incomplete Work

The story could not be completed because development resources were temporarily redirected to resolve a dependency issue involving reporting API approval. As a result, the team prioritized higher-value reporting features and deferred the remaining enhancement to the next sprint.

Sprint Velocity

Planned Story Points

34 Story Points

Completed Story Points

28 Story Points

Sprint Velocity

28 Story Points

The team completed approximately 82% of the planned sprint capacity.

Key Decisions Made During Sprint 2

1. Prioritize reporting functionality over lower-priority enhancement work.
 2. Escalate reporting API approval to stakeholders to reduce dependency delays.
 3. Convert stakeholder feedback from the Sprint Review into future backlog items.
 4. Carry incomplete enhancement work into Sprint 3 rather than extending Sprint 2.
-

Carry-Over Items to Sprint 3

Item	Story Points	Reason
Expense Categories Enhancement	3	Incomplete during Sprint 2
Category Spending Chart	5	Added from Sprint Review feedback
PDF Report Export	5	Added from Sprint Review feedback
Advanced Date Filters	3	Added from Sprint Review feedback

Sprint Outcome

Sprint 2 was largely successful. Most planned functionality was delivered, reporting capabilities were significantly improved, and stakeholder feedback was collected through the Sprint Review process. Although one story was not completed due to dependency-related delays, the issue was identified, managed, and incorporated into Sprint 3 planning.

Overall Sprint Status: **Successful with Minor Carry-Over Work**
